Site HOTO Report — SYL_X0257

Project Tiger · Dhaly Infratech → Alliance Computers Limited · Generated 08-Nov-2026 03:32 BD time

73%	15/15	2	2	11
FORM COMPLETION	CHECKLIST OK	OPEN SNAGS	TOTAL SNAGS	PHOTOS ATTACHED

Incomplete: the following expected fields were left blank in this submission — Site Type, BTS Type, Site Sharing.

SITE & HANDOVER DETAILS

SITE CODE	SYL_X0257	ZONE	Sylhet
HOTO DATE	2026-09-03	DISTRICT	Moulavibazar
HANDOVER ORG	Dhaly Infratech	TAKEOVER ORG	Alliance Computers Limited
HANDOVER PERSON	Omar Faruk	TAKEOVER PERSON	Sourav
HANDOVER PHONE	01406394566	TAKEOVER PHONE	01847426870
INSPECTED BY	sourov sarkar	SECURITY GUARD	No
ACCESS KEY HANDED OVER	—	SITE TYPE	Not Filled
BTS TYPE	Not Filled		
SHARED WITH OPERATOR	Not Filled	SHARED OPERATOR NAME	—

GENERATOR INFORMATION

DG BRAND	FG Wilson	GENSET ASSET NO.	No
CAPACITY (KVA)	22	TYPE	Can
FUEL TANK CAPACITY	2000	PRESENT RH	633
FUEL (NO WATER)	223 L	FUEL (TOTAL)	223 L
WATER AMOUNT	— L	FUEL AMOUNT (WORD)	Two Hundred Twenty Three Liters
DG SITE TYPE	Standard	DG LOCKED AFTER FUELING	Yes
DG PRESENT STATUS	OK	GENSET ON ALARM	OK
BATTERY BRAND	Volvo	BATTERY SERIAL	27MB0579
BATTERY AH	100	ENGINE SERIAL	N844L2216M5260
ATS BRAND	Local	ATS MODE	Auto
RH METER TYPE	Digital from controller	LAST SERVICE DATE	2026-05-08
KEY TYPE	Local Key	KEY STATUS — BTS	Abloy
KEY STATUS — DG ROOM	Open space		

ACTIVE DG	1	CONNECTED FUEL TANKS	1
FAULTY/DISCONNECTED DG	—	FAULTY/DISCONNECTED TANKS	—

CONNECTED GENERATOR CHECKLIST & READINGS

ITEM	VALUE	ITEM	VALUE
Earth Connection OK	Yes	Load Current (A)	24
Frequency (Hz)	50.2	Phase	3 Phase
Output	24	Voltage L1-L2	389
Voltage L2-L3	380	Voltage L3-L1	385
Voltage L1-N	220	Voltage L2-N	215
Voltage L3-N	215	Current Line 1	8
Current Line 2	8	Current Line 3	8
Engine Brand	Perkins	Controller Status	OK
Black Smoke Status	OK	DG Battery Charger	OK
ATS Physical & Functional Status	OK	DG Automation (VDTC/RVDTC/Rectifier) per BL Standard	OK
Fuel Preserved at Safe & Appropriate Location	OK	Exhaust Fan / Ventilation Sufficient When Running	OK
Sufficient Water in Radiator & Battery	OK	DG Radiator Condition	OK
DG Battery Condition	OK	DG Runs in Both Auto & Manual Mode	OK
GENSET ON Alarm Functioning Properly	OK	Lub Oil Status (Level & Colour)	OK
DG RH Meter Working Properly	OK	No Parts Missing (if missing, note in snags below)	OK

SNAGS FOUND (2)

SNAG #	SYSTEM	CATEGORY	COMPONENT	STATUS	OBSERVATIONS	ACTION	PHOTO
S-013	DG	DG - Other	Hi temp sensor	Faulty	—	Open	—
S-014	DG	DG - Other	DG Rusty	Faulty	—	Open	

DEFICIENCIES & SAFETY REMARKS

DG MAJOR DEFICIENCIES	—
SAFETY REMARKS	—
GENERAL REMARKS	—


SITE PHOTOS



Site / Nameplate



DG RH / Meter



Fuel Gauge



Additional



Additional



Additional



Additional



Additio

Omar Faruk
Handed Over By · Dhaly Infratech
01406394566

Date: _____

Sourav
Taken Over By · Alliance Computers Limited
01847426870

Date: _____

BL Concern · Name / Signature

Date: _____

APPENDIX — PHOTO EVIDENCE (11)

Full-size reference photos for SYL_X0257, grouped by type and numbered for cross-reference against the tables above.

REQUIRED SITE PHOTOS (3)



Photo 1 — Site / Nameplate



Photo 2 — DG RH / Meter



Photo 3 — Fuel Gauge

SNAG EVIDENCE PHOTOS (1)



Photo 4 — S-014 — DG Rusty

ADDITIONAL PHOTOS (7)



Photo 5 — Additional Photos 1



Photo 6 — Additional Photos 2



Photo 7 — Additional Photos 3



Photo 8 — Additional Photos 4



Photo 9 — Additional Photos 5



Photo 10 — Additional Photos 6

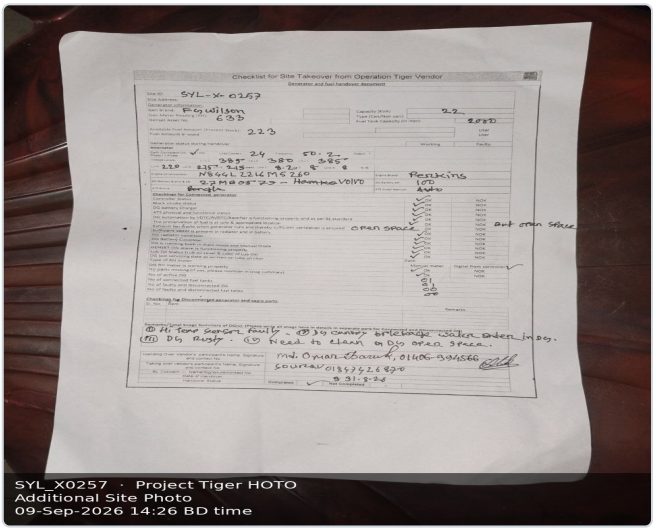


Photo 11 — Additional Photos 7
